

Desire-Florida Multi-Service Center

New Orleans Recreation Development Commission (NORDC)

Monthly Commission Meeting - April 5, 2022


Prepared by the City of New Orleans, Capital Projects Administration



NORD Capital Program

Phase	No. of Projects	% Projects	Budget	% Budget
Complete	22	45%	\$22,739,665	44%
Construction	4	9% \$7,475,424		14%
Bid & Award	11	24%	\$7,510,519	15%
Design	3	6%	\$5,120,315	10%
Pre-Design	7	15%	\$9,094,025	16%
On Hold	1	1%	\$368,421	1%
	48		\$52,308,369	



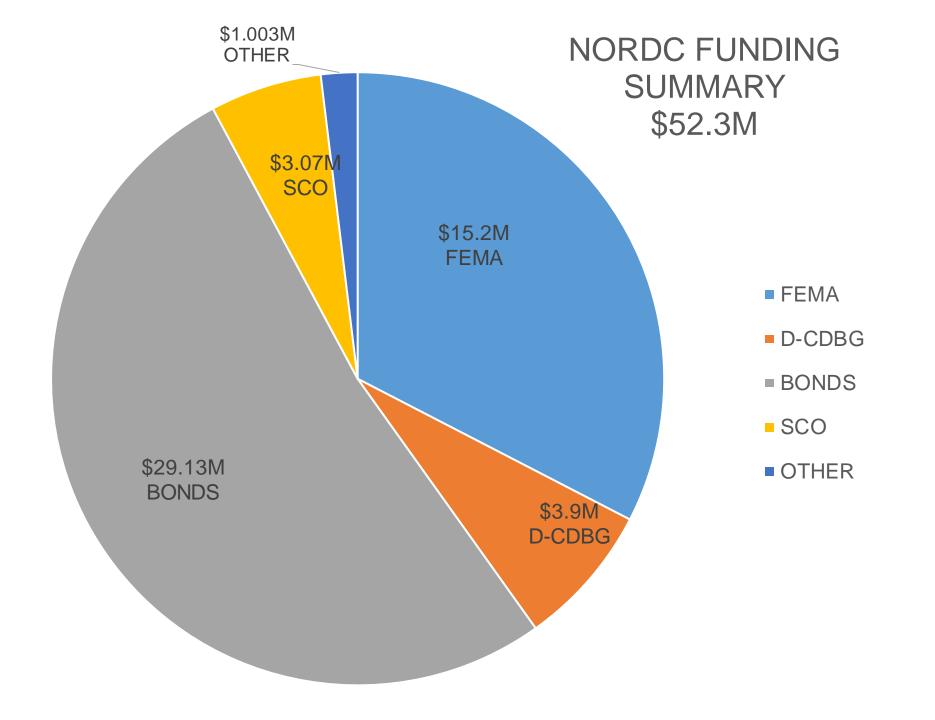

NORD Capital Projects - Complete (22)

	Project Name	District	Completed
1	Village De L'est Community Building & Park	E	Q1-2022
2	Lambert Park Walking Path	С	Q4-2020
3	Huff Park Walking Path	С	Q4-2020
4	Collins Park Walking Path	С	Q42020
5	Lafitte Greenway Concessions/Restroom Bldg.	D	Q4-2020
6	East Shore Playground Multi-Purpose Center	Е	Q4-2020
7	Donsereaux/Harrison Playground Fencing	С	Q4-2020
8	Delgado Playground (FEMA Repairs)	Α	Q3-2019
9	Bertha Maugrauer Center Demolition	D	Q3-2019
10	Norman Playground (Equipment)	С	Q4-2019
11	Lafitte Greenway Shelter at Lopez St. Brake Tag Station	В	Q1-2020
12	McCue Playground Improvements	D	Q1-2020
13	Cuccia-Byrnes Playground	Α	Q2-2019



NORD Capital Projects - Complete (22)

	Project Name	District	Completed
14	Bodenger Playground	С	Q2-2019
15	Kerry Curley Playground Improvements	Е	Q2-2019
16	Bunny Friend Playground Improvements	D	Q2-2019
17	Kenilworth Playground Improvements (Misc. Park Improvements)	E	Q4-2018
18	Hunter's Field Phase III - New Building Addition	D	Q3-2018
19	West Bank Natatorium (Design Only)	С	Q2-2018
20	Hardin Playground Improvements	D	Q3-2018
21	Gert Town Community Pool	В	Q2-2018
22	Behrman Park Improvements	С	Q2-2018



NORD Capital Projects – Complete (1)

		_		
Project Name	District	Bid Receive Date	Anticipated Const. Start	
Village de L'est Playground Phase II – Community Building & Park Improvements (\$2M) Bonds Construction of new 1,500 concession, restroom and storage building. [The Construction Phase is complete.]	E	August 6, 2020A	1/18/21A	Q1-2022







Project Name	District	Bid Receive Date	Anticipated Const. Start	Anticipated Completion
Alma Peters Playground Improvements (\$170K) SCO Miscellaneous Park Improvements for safety and accessibility. [The Construction Phase is currently in Progress at 55% complete. Demolition is currently in progress.]	А	June 24, 2021A	11/29/21A	Q2-2022







Project Name	District	Bid Receive Date	Anticipated Const. Start	Anticipated Completion
Desire / Florida Multi-Purpose Center (\$6.5M) FEMA Construction of a new 11,000 sq. ft. Multi-Purpose/Senior Center [The Construction Phase is in progress. The contractor received open wall inspection on 3/18 and is completing installation of the roof panels. The next milestone is to receive permanent power.]	D	August 6, 2020A	2/8/21A	Q2-2022








Project Name	District		-	Anticipated Completion
Citywide Parks and Playground Improvements Package #3 (SAMPSON PLAYGROUND) (\$235K) SCO Installation of new basketball court and new playground safety surface [The Construction Phase is currently in progress. The contractor completed selective playground demolition work at Sampson.]		June 29, 2021	1/14/22A	Q3-2022



SAMPSON PLAYGROUND: Materials












Project Name	District	Bid Receive Date	Anticipated Const. Start	Anticipated Completion
Citywide Parks and Playground Improvements Package #3 (BOE PLAYSPOT) (\$165K) SCO Installation of new 2-5 yr. old playground equipment [The contractor is forming/pouring concrete sidewalks. Playground equipment for Boe Playground has been ordered.]	CW	June 29, 2021	1/14/22A	Q3-2022







Project Name	District	Bid Receive Date	Anticipated Const. Start	Anticipated Completion
Citywide Parks and Playground Improvements Package #3 (PEACE PLAYSPOT) (\$40K) SCO Installation of perimeter fencing and NORD C Playground sign [The contractor is mobilizing their workforces.]	CW	June 29, 2021	1/14/22A	Q3-2022

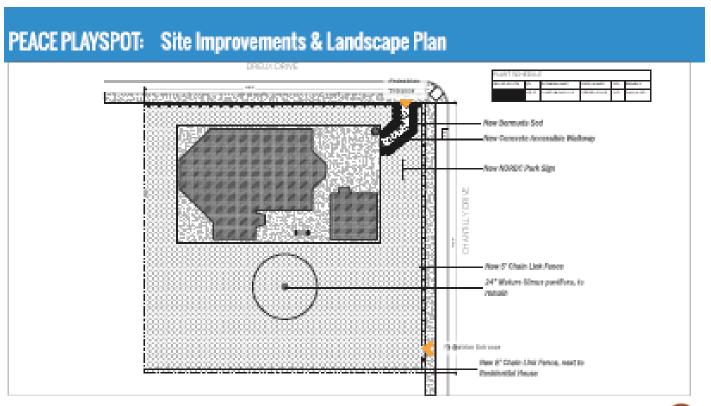




Project Name	District	Bid Receive Date	Anticipated Const. Start	Anticipated Completion
Pratt Playground (\$365K) SCO Canopy installations at the Gazebo and Existing Play Structure [The Construction Phase is currently in progress. The contractor completed concrete work and is currently waiting for the delivery of playground materials.]	D	August 22, 2021	2/1/22	Q3-2022







Project Name	District	Bid Receive Date		Anticipated Completion
Cut-Off Recreation Center Splash Pad & Walking Trail (\$489K) SCO/Bonds Installation of a splash pad and walking trail at the Cut-off Recreation Center [The Bid Phase is in progress. The project has been posted for rebid and the pre-bid conference was 3/25/22 at 2:30pm. The next milestone is to receive bids on 4/8/22.]	С	April 8, 2022	6/7/22	Q4-2022

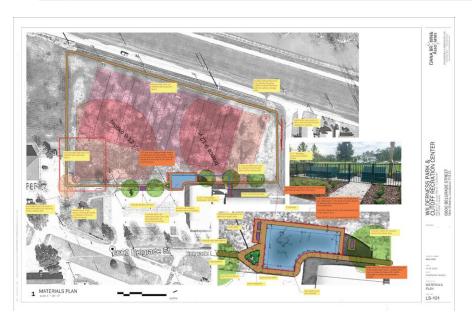





Project Name	District	Bid Receive Date	Anticipated Const. Start	Anticipated Completion
Easton Playground – Isaac HML Repairs (\$33K) FEMA The scope is repair of HML lighting per Hurricane Isaac PW 526. [The Bid and Award Phase is in progress. The construction contract is currently routing for approval and acceptance.]	А	N/A	4/1/22	Q2-2022







Project Name	District	Bid Receive Date	Anticipated Const. Start	· ·
George Washington Carver Playground Improvements – Zone A (\$188K) Bonds/SCO Ballfield and Misc. Park Improvements [The Bid and Award Phase is currently in progress. The bid opening (re-bid) is scheduled for April 27, 2022.]	A	April 27, 2022	6/26/2022	Q3-2022



G.W. CARVER PLAYGROUND IMPROVEMENTS, ZONE A

NEW ORLEANS, LA FOR CITY OF NEW ORLEANS, CAPITAL PROJECTS ADMINISTRATION

IDDING S 3-01-2021									PROJECT #: NRD 22 FP&C No. 50-ML3-19-0
INITY MAP - 1"+	100.	LEMEANDES		DRAWING	INDEX -	ZONI	A		ALTERNATES:
			SHEET NAMEDS	SPEET NAME	PROGRAMMAG	90	00 C0	BECOME	CONTRACTOR TO ACCITUDE FOLLOWING
-) N		200 B N.IC. 0 0	me						1 SEMBLE ONE EXCENS HIS HIGH WAS LIGHT POLY AND HIS ASSOCIATED POLYTING WINNING HIS MANY LIGHT PROTEST AND AND AND CONTEST.
/ /	1		THIA THE	en					PET HISCAND PETURE TO OWNER SCOURCE LINES WHIREASS PETURES AND PETURE TO OWNER SCOURCE LINES WHIREASS.
/			GREAT TERM	211403547600					2 CONSTRUCT AND RETAIL TWO PIELS INGREETED DIGGST ORIGINES AND AGRICULTUS FORTINGS
/			20000						8 PROVIDE BYOP DRAWINGS (FAMPED BY A LOUGHMA-LICENSED PROFESSIONAL DISINEER.
1	ZONE A		2014 9.6%						
	ZUNE A	1/20	LAMESON'S	NUTON CONCRUTAN					
		1/2/ 1/2/	LINEA STELL	POLE MATERIALS MAD PLANTING PLANT ACTUS LEWIS CO. MATERIAL PLANT	B			- :	
K	/		DEA STEE	SEE			- :	:	
1	N/		MOUTOTHE		10				
Carre Line		(// ////	#85 A \$1000	ONORG					
7/2	3								
REASTE NEXT HAS ALSO AND A REASTE NOT AN		PROJECT DESCRIPTION	PROJEC	CT DIRECTO	RY				
UNICIPAL LOCA	P.CHR.E	THE PROJECT RELIGIES APPROVEMENTS TO THE EXCERNIG SACREAL FIELD IT WILL BE RE-GRADED AND SCORED NEW	5-5	T DIRECTO		ECT			
A BLOG AREA + NOT AN	TION OF PROJECT	THE MOLE OF RELUES APPROXEMENTS TO THE EXCEND MARRISH THE B. IT THE LIKE THE OWNER SECTION OF THE LIKE THE CHARLES MAY BE ANNOTHING THE OWNER SECTION OF THE CHARLES MAY BE ANNOTHED WHILL BETWEEN THE	OWNER	CWYTH, PROJECTS ADMINISTRATE	ARCHII IN IOLOTI	×			
BLOG HIER + NOT AN NICIPAL LOCA 1008	TION OF PROJECT JAIN PROVINGE STREET HER CREEKE, LA PRIM	THE PROJECT RECURSE ANYONEMENTS TO THE EXCEPTION SHOULD SHE THE CONTINUE SHOULD SHE SHOULD SHOULD SHE SHOULD SHOULD SHE SHOULD S	OWNER CITY OF NEW CHLORIE JOHNSON OF CITY 1800 FERRORS ST. CITY MY TRESON ST. CITY	CONTRAL PROJECTS ACMENISTRATE REMOGRAT MALL SHATE SETS	ARCHII IN TOLE OFF MENORIA	TE RET. BATE 20 ME. (x 7910)			
LOG BREE + NOT AN ICIPAL LOCA IN. E NAMEDI	TION OF PROJECT JALL PROVIDED STREET HER ORIGING, LA TYLES 204 106	THE PROOF OF RELIEFS ANY REMAINS TO THE CONTINUE ASSESSMENT FROM THE RE-OWNERS HAVE COURSE WAS ASSESSMENT FROM THE RE-OWNERS HAVE COURSE WAS ASSESSMENT OF THE RE-OWNERS OF THE RE-OWNERS OF THE PROOF O	OWNER OTY OF NEW CREAMS STREET, CREATED	CONTRAL PROJECTS ACMENISTRATE REMOGRAT MALL SHATE SETS	ARCHII IN TORE OTT	TE RET. BATE 20 ME. (x 7910)			
ROSENIA - HOTAL NICIPAL LOCA TOS TOS TOS TOS TOS TOS TOS TO	TION OF PROJECT JUST PROVIDER STREET 1998 ORGANIC, LA TYTE 200 100 100 100 100 100 100 100 100 100	THE MODELLY REQUEST. ANY OWN MATTER TO THE COSTINUE MATERIAL THE LITE OF OWN CONCESS ON MATERIAL THE LITE OF OWN CONCESS ON ELEMANTO DIRECTOR OF CONCESS ON MATERIAL TO CONCESS ON MATE	OWNER CITY OF NEW CHLORIE JOHNSON OF CITY 1800 FERRORS ST. CITY MY TRESON ST. CITY	CONTRAL PROJECTS ACMENISTRATE REMOGRAT MALL SHATE SETS	ARCHIT 506 5095 017 609 107 609 016 -1396 33	TE RET. BATE 20 ME. (x 7910)			
E A BLOG MRIER - HOT AN UNICIPAL LOCA EFFORE LUPES HAMBOR TO NAMEDR TOWNSELL MRIER M	TION OF PROJECT JALL PROVIDED STREET HER ORIGING, LA TYLES 204 106	THE PROOF OF RELIEFS ANY REMAINS TO THE CONTINUE ASSESSMENT FROM THE RE-OWNERS HAVE COURSE WAS ASSESSMENT FROM THE RE-OWNERS HAVE COURSE WAS ASSESSMENT OF THE RE-OWNERS OF THE RE-OWNERS OF THE PROOF O	OWNER OTHER GLORI (BHILLOS FROSCO (BRORFROSO ST. OTHER (BURNESSA), LE TOTA (1) (SECTOR 2008	CONTRAL PROJECTS ACMENISTRATE REMOGRAT MALL SHATE SETS	ARCHIT 506 5095 017 609 107 609 016 -1396 33	EST BATE PO ME DA 79130 1538 CAPE ARC			





Project Name	District	Bid Receive Date	Anticipated Const. Start	Anticipated Completion
George Washington Carver Playground Improvements – Zone B (\$629K) Bonds/SCO Ballfield and Misc. Park Improvements [The Bid and Award Phase is currently in progress. The bid package has been submitted to Purchasing to begin advertisement of re-bid. The project bid opening date is 5/5/2022.]	А	May 5, 2022	7/14/22	Q4-2022



Project Name	District	Bid Receive Date		Anticipated Completion
Hunter's Field Phase IV (\$385k) Bonds Renovations to the existing building to create a functioning activity space [The Bid and Award Phase (re-bid) is currently in progress. The contract package will begin routing to Purchasing the week of 3/28/22.]	D	November 18, 2021	05/7/22	Q3-2022





Project Name	District	Bid Receive Date	Anticipated Const. Start	Anticipated Completion
Morris FX Jeff Pool Renovations (\$4.5M) CDBG/FEMA/Bonds Enclose and expansion of pool amenities [The Bid and Award Phase is currently in progress. The bid package has been submitted for routing to Purchasing to begin Procurement. Plans have been submitted for SFM and Building Permit review and approval.]	C	May 1, 2022	06/30/22	Q2-2023














VIEW FROM LOCKER ROOMS TO POOL DECK



Project Name	District		•	Anticipated Completion
NORDC Hurricane Isaac Repairs (\$97K) Misc. FEMA-Hurricane Isaac Repairs and various NORD sites. [The Bid and Award Phase is currently in progress. The (4) bid packages are currently being advertised. The bid opening date for all (4) packages is 4/1/22.]	CW	April 1, 2022	05/31/22	Q3-2022

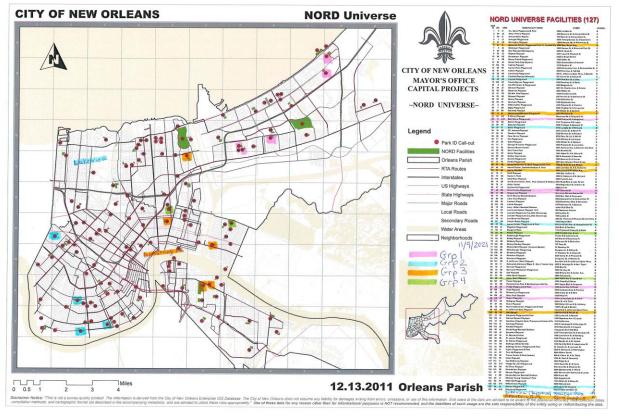




Project Name	District	Bid Receive Date	Anticipated Const. Start	Anticipated Completion
Norman Playground - Play Equipment Phase II (\$350K) Bonds Installation of play equipment for children ages 5 to 12 years old [The Bid and Award Phase is currently in progress. The bid opening is scheduled for April 7, 2022.]	С	April 7, 2022	07/8/22	Q1-2023





Project Name	District	Bid Receive Date	Anticipated Const. Start	Anticipated Completion
Treme Elevator (\$565K) SCO/Bonds Installation of a new elevator at the Treme Recreation Center. [The Bid and Award Phase is currently in progress. The bid package is currently routing to Purchasing to begin procurement. The City is also waiting for FP&C approval of the bid package.]	С	May 11, 2022	06/10/22	Q4-2022

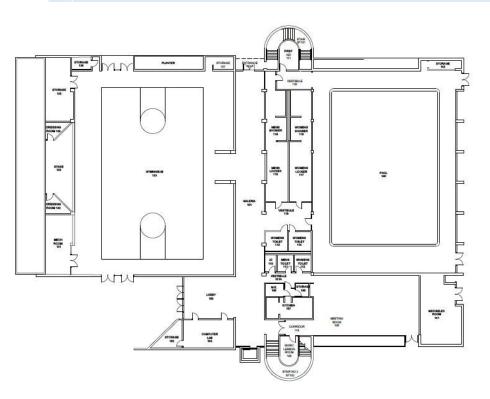








1 EXTERIOR ELEVATION - NORTH FACE - NEW WORK SCHEINSE





	Project Name	District	Bid Receive Date		Anticipated Completion
	Audubon Fly Park Improvements (\$98K) SCO Miscellaneous park improvements at Avenger Baseball fields [The Bid and Award Phase is currently in progress. The project will be procured thru the Informal bid process.]	А	April 22, 2022	07/6/22	Q4-2022

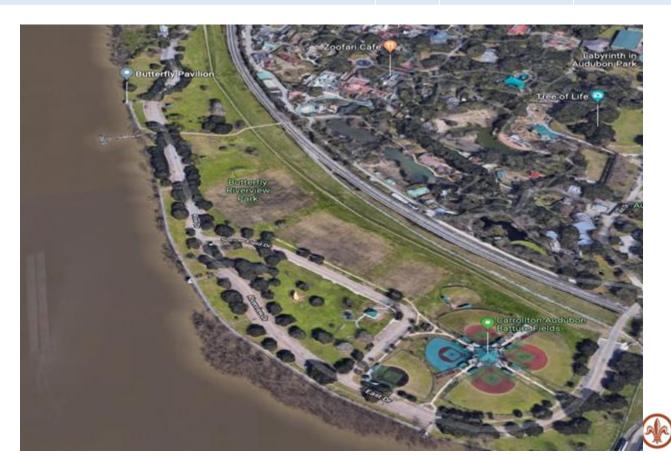

CITY OF NEW ORLEANS MAYOR LATOYA CANTRELL

Project Name	District	Bid Receive Date	Anticipated Const. Start	Anticipated Completion
Harold Gene Devore Playground Renovations (\$110K) Bonds Miscellaneous park improvements [The Bid and Award Phase is currently in progress. The bid opening is scheduled for 4/1/22.]	С	April 1, 2022	05/31/22	Q3-2022





NORD Capital Projects - Design (3)

Project Name	District	Design Phase Completion
Morris FX Jeff Ball Field Renovations (\$362K) Bonds Improvements to existing baseball fields [The Design Phase is currently in progress. SD/DD Plans are currently under review.]	С	Q2-2022







NORD Capital Projects - Design (3)

Project Name	District	Design Phase Completion
Skelly Rupp Stadium Repairs (\$4.3M) Bonds Miscellaneous park improvements [The Design Phase is currently in progress. Construction Documents are being prepared. Hurricane ZETA and IDA scopes of work have been identified to incorporate into the project. The 95% CD package is currently under review.]	С	Q2-2022





Project Name	District	Design Phase Completion
Wesley Barrow Stadium Multi Purpose Bldg. (\$450K) MLB Construction of a new Multi-Purpose Building [The Design Phase is in progress. The project was originally designed to use a pre-fabricated modular building to save cost. The modular fabrication company no longer produces the system that was chosen. The architect is examining the options (other pre-fab manufacturers, stick build cost).]	D	Q2-2022





Project Name	District	Pre-Design Phase Completion
Perry Roehm Stadium Improvements (\$568K) Bonds Miscellaneous park improvements at Avenger Baseball fields. [The Pre-Design phase is currently in progress. The design contract is being routed for execution.]	D	Q2-2022





Project Name	District	Pre-Design Phase Completion
Easton Playground Basketball Court (\$277k) Bonds Renovations to the Concessions/Restroom Bldg; Refurbish Half-Basketball Court [The Pre-Design phase is currently in progress. CPA is meeting w/NORDC to confirm the proje scope.]	ct A	Q2-2022





Project Name	District	Pre-Design Phase Completion
Odile Davis Park Improvements (\$500K) Bonds Misc. Park Improvements [The Pre-Design phase is currently in progress. CPA will meet with NORDC to develop a project scope and budget and will prepare an RFP for AE services.]	D	Q2-2022





Project Name	District	Pre-Design Phase Completion
Sampson Playground Improvements (\$500k) Bonds Miscellaneous Improvements that include renovations to the pool house, rehab of the existing pavilion, resurfacing basketball court and new play equipment. [The Pre-Design phase is currently in progress. CPA will meet with NORDC to develop a project scope and budget and will prepare an RFP for AE services.]	А	Q2-2022





Project Name	District	Pre-Design Phase Completion
Pecan Grove Recreation Center (\$3.3M) Bonds Interior renovations to the existing HANO Owned Pelican Grove Building to accommodate a new community center. The building is currently being used as a warehouse storage building by NORD. [The Pre-Design Phase is currently in progress. CPA has met with NORDC to develop a scope & project budget. Scoping docs will be transmitted to NORDC for approval and the procurement package will be developed.]	D	Q2-2022






Project Name	District	Pre-Design Phase Completion
Richard Lee Playground Improvements (Ph 1) (\$2.5M) Bonds Design of Phase I improvements from the master plan [The Pre-Design Phase is currently in progress. CPA has met with NORDC to develop a scope & project budget. Scoping docs will be transmitted to NORDC for approval and the procurement package will be developed.]	А	Q2-2022





Project Name	District	Pre-Design Phase Completion
Village De L'est Splash Pad (\$600K) Bonds Installation of a splash pad at the Village De L'est Playground site. [The Pre-Design phase is currently in progress. CPA will meet with NORDC to develop a project scope and budget and will prepare an RFP for AE services.]	E	Q2-2022

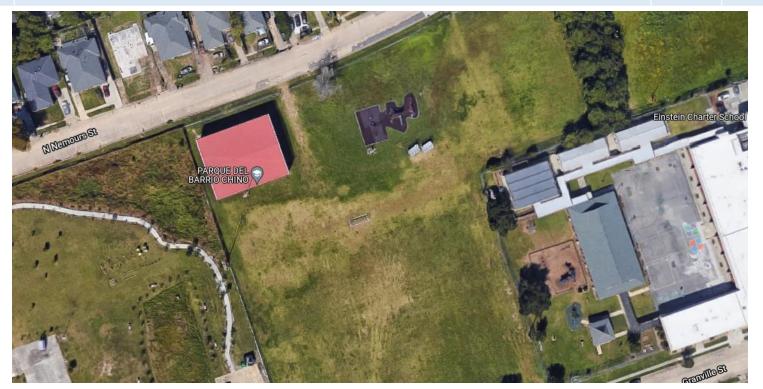



NORD Capital Projects - ON HOLD (1)

Project Name	District	Design Phase Completion
Gernon Brown Recreation Center (\$368K) SCO Installation of new playground equipment and Basketball court refurbish [Design is complete. Waiting for execution of the CNO/City Park CEA agreement]	А	TBD

